

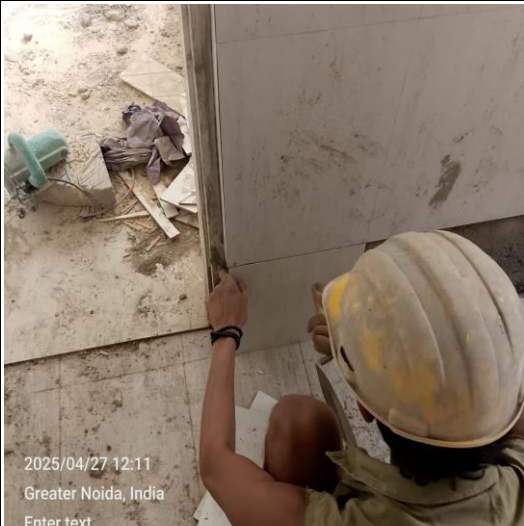







Sikka Kaamya Project

Progress Report for the period 28-04-2025 to 04-05-2025

	Tower Photo	Item	Progress of work
DIAMOND		RMC/Steel	13th floor columns / shear wall shuttering work in progress - 2nd pour
		Paint	Internal paint to start this week
		Tiling	1st floor completed
		Plumbing	1st floor completed
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	5th floor in progress
		External Plaster	N/A
		Fire Fighting	Yet to start
RUBY	 2025/04/27 11:41 Greater Noida, India Enter text © TECNO	RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 60%
		Tiling	Bedroom Floor Tiling at 14th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	95% completed
Fire Fighting	Internal sprinkler system piping completed		
OPAL	 2025/04/27 12:11 Greater Noida, India Enter text	RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 55%
		Tiling	Toilet Wall tile fixing at 13th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
External Plaster	90% completed		

		Fire Fighting	Internal sprinkler system piping completed
JADE		Brickwork / RMC	Lift shaft brickwork in progress
		Paint	Internal putty work completed, external primer done 50%
		Tiling	Toilet Floor Tiling at 12th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed -90%
		External Plaster	Scaffolding work for external plaster in progress
		Fire Fighting	Internal sprinkler system piping in progress
AMBER		RMC	Structure Work Completed
		Paint	Internal putty work completed, external primer done 62%
		Tiling / Granite work	Floor Tiling for master bedroom at 21st floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Lift lobby internal plaster - 21st floor
		External Plaster	Over Head Tank plaster completed and curing works in progress
Fire Fighting	Internal sprinkler system piping completed		
SAPPHIRE		RMC	Structure Work Completed
		Paint	Internal putty work completed, external painting done 80%
		Tiling	Lift Wall Tile Cladding at 21st floor in progress
		Plumbing	Completed
		Electrical	Conduit work completed, wiring work in progress
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
Fire Fighting	Completed		

PEARL		RMC	Structure Work Completed
		Paint	Completed, final coat balance
		Tiling	Completed
		Plumbing	Completed
		Electrical	Completed
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		W/proofing	Waterproofing of NTA area around Pearl tower
EMERALD		RMC/Steel	6th floor Columns & Shear walls R/F fixing in progress - 2nd pour
		Paint	Yet to start
		Tiling	Yet to start
		Plumbing	Yet to start
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	Yet to start
		External Plaster	N/A
		Fire Fighting	Yet to start
