






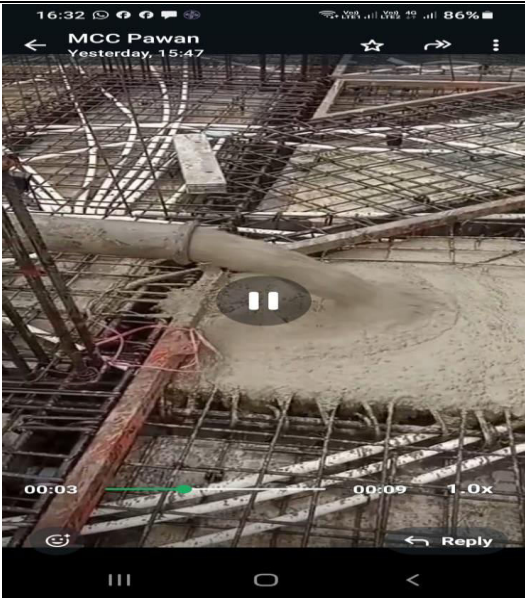


Progress Report for the period 12-05-2025 to 18-05-2025

	Tower Photo	Item	Progress of work
DIAMOND		RMC/Steel	14th floor Reinforcement work in progress - 1st pour
		Paint	Internal paint to start this week
		Tiling	1st floor completed
		Plumbing	1st floor completed
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	5th floor in progress
		External Plaster	N/A
		Fire Fighting	Yet to start
RUBY		RMC	Structure Work Completed
		Paint	Internal putty work completed, external primer done 60%
		Wall Tiling	Lift wall tile cladding at 8th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	95% completed
		Fire Fighting	Internal sprinkler system piping completed
OPAL		RMC	Structure Work Completed
		Paint	Internal putty work completed, external primer done 55%
		Tiling	Toilet Wall tile fixing at 18th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	

		Fire Fighting	Internal sprinkler system piping completed
JADE		Brickwork / RMC	Lift shaft brickwork in progress
		Paint	Internal putty work completed, external primer done 50%
		Tiling	Toilet Floor Tiling at 17th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed -90%
		External Plaster	Scaffolding work for external plaster in progress
		Fire Fighting	Internal sprinkler system piping in progress
		AMBER	
Paint	Internal putty work completed, external primer done 62%		
Tiling / Granite work	Granite Flooring for Staircase at 15th floor in progress		
Plumbing	Internal water supply and drainage work completed		
Electrical	Conduit work completed, wiring work yet to start		
M.S. Railings	Balcony railing completed and staircase railing in progress		
Internal Plaster	Lift lobby internal plaster - 21st floor		
External Plaster	Over Head Tank plaster completed and curing works in progress		
Fire Fighting	Internal sprinkler system piping completed		
SAPPHIRE		RMC	Structure Work Completed
		Paint	Internal putty work completed, external painting done 80%
		Tiling	Lift Wall Tile Cladding at Basement Floor in progress
		Plumbing	Completed
		Electrical	Conduit work completed, wiring work in progress
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	External plaster of one flat in progress
Fire Fighting	Completed		

PEARL		RMC	Structure Work Completed
		Paint	Completed, final coat balance
		Tiling	Completed
		Plumbing	Completed
		Electrical	Completed
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		W/proofing	Waterproofing of NTA area around Pearl tower
EMERALD		RMC/Steel	7th floor Slab casting in progress - 1st pour
		Paint	Yet to start
		Tiling	Yet to start
		Plumbing	Yet to start
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	Yet to start
		External Plaster	N/A
		Fire Fighting	Yet to start
