
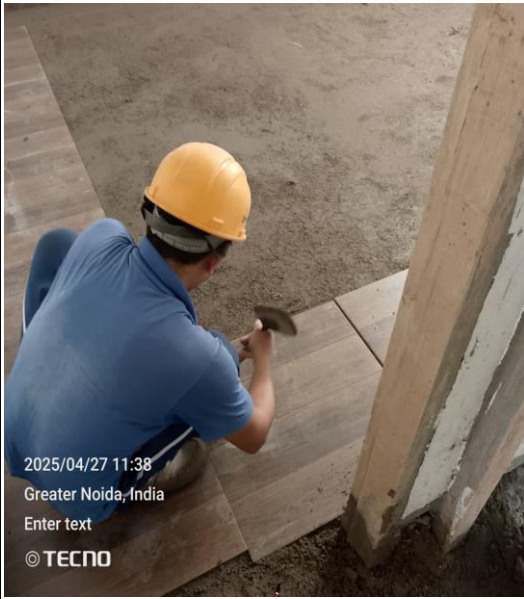
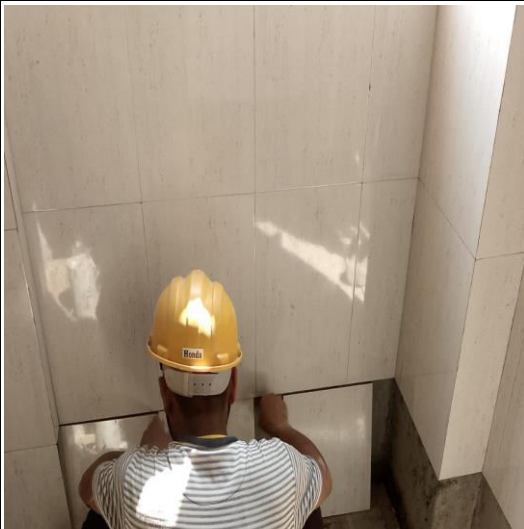








**SIKKA KAAMYA PROJECT - PROGRESS REPORT - 02-06-2025 to 08-06-2025**

	Tower Photo	Item	Progress of work
DIAMOND		<b>RMC/Steel</b>	<b>14th floor Shuttering work in progress - 2nd pour</b>
		Paint	Internal paint to start this week
		Tiling	1st floor completed
		Plumbing	1st floor completed
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	5th floor in progress
		External Plaster	N/A
		Fire Fighting	Yet to start
RUBY		RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 60%
		<b>Tile Work</b>	<b>Master Bedroom flooring at 20th floor in progress</b>
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	95% completed
Fire Fighting	Internal sprinkler system piping completed		
OPAL		RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 55%
		<b>Tiling</b>	<b>Toilet Wall tile fixing at 20th floor in progress</b>
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	

		Fire Fighting	Internal sprinkler system piping completed
JADE		Brickwork / RMC	Lift shaft brickwork in progress
		Paint	Internal putty work completed, external primer done 50%
		<b>Tiling</b>	<b>Toilet Floor Tiling at 15th floor in progress</b>
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed -90%
		External Plaster	External plaster work in progress
		Fire Fighting	Internal sprinkler system piping in progress
		AMBER	
Paint	Internal putty work completed, external primer done 62%		
Tiling / Granite work	Toilet tile Flooring at 14th floor level in progress		
Plumbing	Internal water supply and drainage work completed		
Electrical	Conduit work completed, wiring work yet to start		
M.S. Railings	Balcony railing completed and staircase railing in progress		
Internal Plaster	Lift lobby internal plaster - 21st floor		
<b>External Plaster</b>	<b>External plaster work in progress</b>		
Fire Fighting	Internal sprinkler system piping completed		
SAPPHIRE		RMC	Structure Work Completed
		Paint	Internal putty work completed, external painting done 80%
		Tiling	Lift Wall Tile Cladding at Basement Floor in progress
		<b>Plumbing</b>	<b>Terrace GI Ring line completed</b>
		Electrical	Conduit work completed, wiring work in progress
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	External plaster of one flat in progress
Fire Fighting	Completed		

PEARL		RMC	Structure Work Completed
		Paint	Completed, final coat balance
		Tiling / Granite work	Granite skirting fixing work at Reception area
		Plumbing	Completed
		Electrical	Completed
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		W/proofing	<b>Screed done above waterproofing in front of Pearl tower</b>
EMERALD		RMC/Steel	<b>7th floor Reinforcement work in progress - 2nd pour</b>
		Paint	Yet to start
		Tiling	Yet to start
		Plumbing	Yet to start
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	Yet to start
		External Plaster	N/A
		Fire Fighting	Yet to start
