
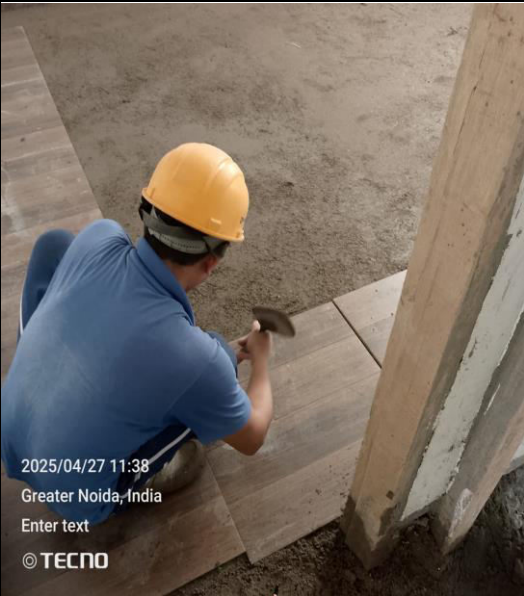







Sikka Kaamya Project

Progress Report for the period 21-04-2025 to 27-04-2025

	Tower Photo	Item	Progress of work
DIAMOND		RMC/Steel	13th floor columns / shear wall shuttering work in progress
		Paint	Internal paint to start this week
		Tiling	1st floor completed
		Plumbing	1st floor completed
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	5th floor in progress
		External Plaster	N/A
		Fire Fighting	Yet to start
RUBY	 <p>2025/04/27 11:38 Greater Noida, India Enter text © TECNO</p>	RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 60%
		Tiling	Master Bedroom Floor Tiling at 13th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	95% completed
		Fire Fighting	Internal sprinkler system piping completed
OPAL	 <p>2025/04/27 12:15 Greater Noida, India Enter text</p>	RMC	Structure Work Completed
		Paint	Intenal putty work completed, external primer done 55%
		Tiling	Toilet Wall tile fixing at 12th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed
		External Plaster	90% completed

		Fire Fighting	Internal sprinkler system piping completed
JADE		Brickwork / RMC	Lift shaft brickwork in progress
		Paint	Internal putty work completed, external primer done 50%
		Tiling	Toilet Floor Tiling at 10th floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Completed -90%
		External Plaster	Scaffolding work for external plaster in progress
		Fire Fighting	Internal sprinkler system piping in progress
AMBER		Paint	Internal putty work completed, external primer done 62%
		Tiling / Granite work	Floor Tiling for master bedroom at 21st floor in progress
		Plumbing	Internal water supply and drainage work completed
		Electrical	Conduit work completed, wiring work yet to start
		M.S. Railings	Balcony railing completed and staircase railing in progress
		Internal Plaster	Lift lobby internal plaster - 21st floor
		External Plaster	Over Head Tank plaster in progress
		Fire Fighting	Internal sprinkler system piping completed
SAPPHIRE		RMC	Structure Work Completed
		Paint	Internal putty work completed, external painting done 80%
		Tiling	Lift Wall Tile Cladding at 20th floor in progress
		Plumbing	Completed
		Electrical	Conduit work completed, wiring work in progress
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		Fire Fighting	Completed

PEARL		RMC	Structure Work Completed
		Paint	Completed, final coat balance
		Tiling	Completed
		Plumbing	Completed
		Electrical	Completed
		M.S. Railings	Completed
		Internal Plaster	Completed
		External Plaster	Completed
		Fire Fighting	Completed
EMERALD		RMC/Steel	6th floor Columns & Shear walls R/F fixing in progress
		Paint	Yet to start
		Tiling	Yet to start
		Plumbing	Yet to start
		Electrical	Yet to start
		M.S. Railings	Yet to start
		Internal Plaster	Yet to start
		External Plaster	N/A
		Fire Fighting	Yet to start
